


## REQUEST FOR INFORMATION

| То:   | Royal Construction   | <u>RFI #</u> | 1                |
|-------|----------------------|--------------|------------------|
|       | 3653 Greenway St.    | Date         | April 23, 2020   |
|       | Eau Claire, WI 54701 |              |                  |
| Attn: | Eric Runner          | Requested By | Stephanie McNeil |
| Re:   | LVL Penetrations     | Title        | Project Manager  |

| Question(s):  |                                     |                    |  |  |  |
|---|-------------------------------------|--------------------|--|--|--|
| On the first floor at Cannery Trail Residences (The Current), Viking will have two penetrations through B4 – LVL in front of the elevator.      |                                     |                    |  |  |  |
| We will need to core (2) 3" holes through the LVL and are requesting authorization to proceed. The location of the LVL is provided as           |                                     |                    |  |  |  |
| a screenshot in the attachment and can also be found on S211: Framing Plan – 2 <sup>nd</sup> Floor. Also attached is Viking's sprinkler drawing |                                     |                    |  |  |  |
| for that floor with a screenshot of the area being discussed. Please let us know where we can core and what requirements need to be             |                                     |                    |  |  |  |
| followed.   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
| Please Respond within: 6 working days from April 23, 2020 to not affect design or installation  |                                     |                    |  |  |  |
| We ☐ Do ☐ Do not Consider this RFI to affect the contract amount or schedule.   |                                     |                    |  |  |  |
| Response(s):  |                                     |                    |  |  |  |
| Holes can be cut at the following locations   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   | 22" 3" 14" 3"                       |                    |  |  |  |
|   |                                     |                    |  |  |  |
| T + +   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
|   |                                     |                    |  |  |  |
| Response by:  | Ryan Schultz and Luis C. Pérez Tato | Date: {4/24/2020 } |  |  |  |

## 1<sup>st</sup> Floor B4 – LVL

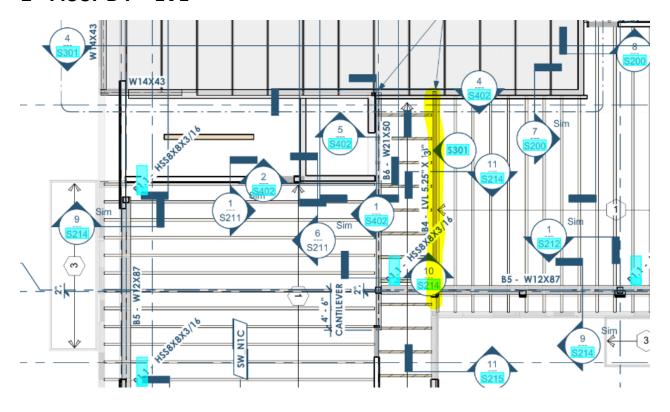

## 1<sup>st</sup> Floor Viking Penetrations

